
Nirmaan.

Website & field PWA

A formal, record-focused interface for connecting field progress to the project schedule.

BITS PILANI

SIH 26122 | Oil India Limited problem statement | 20 September 2026

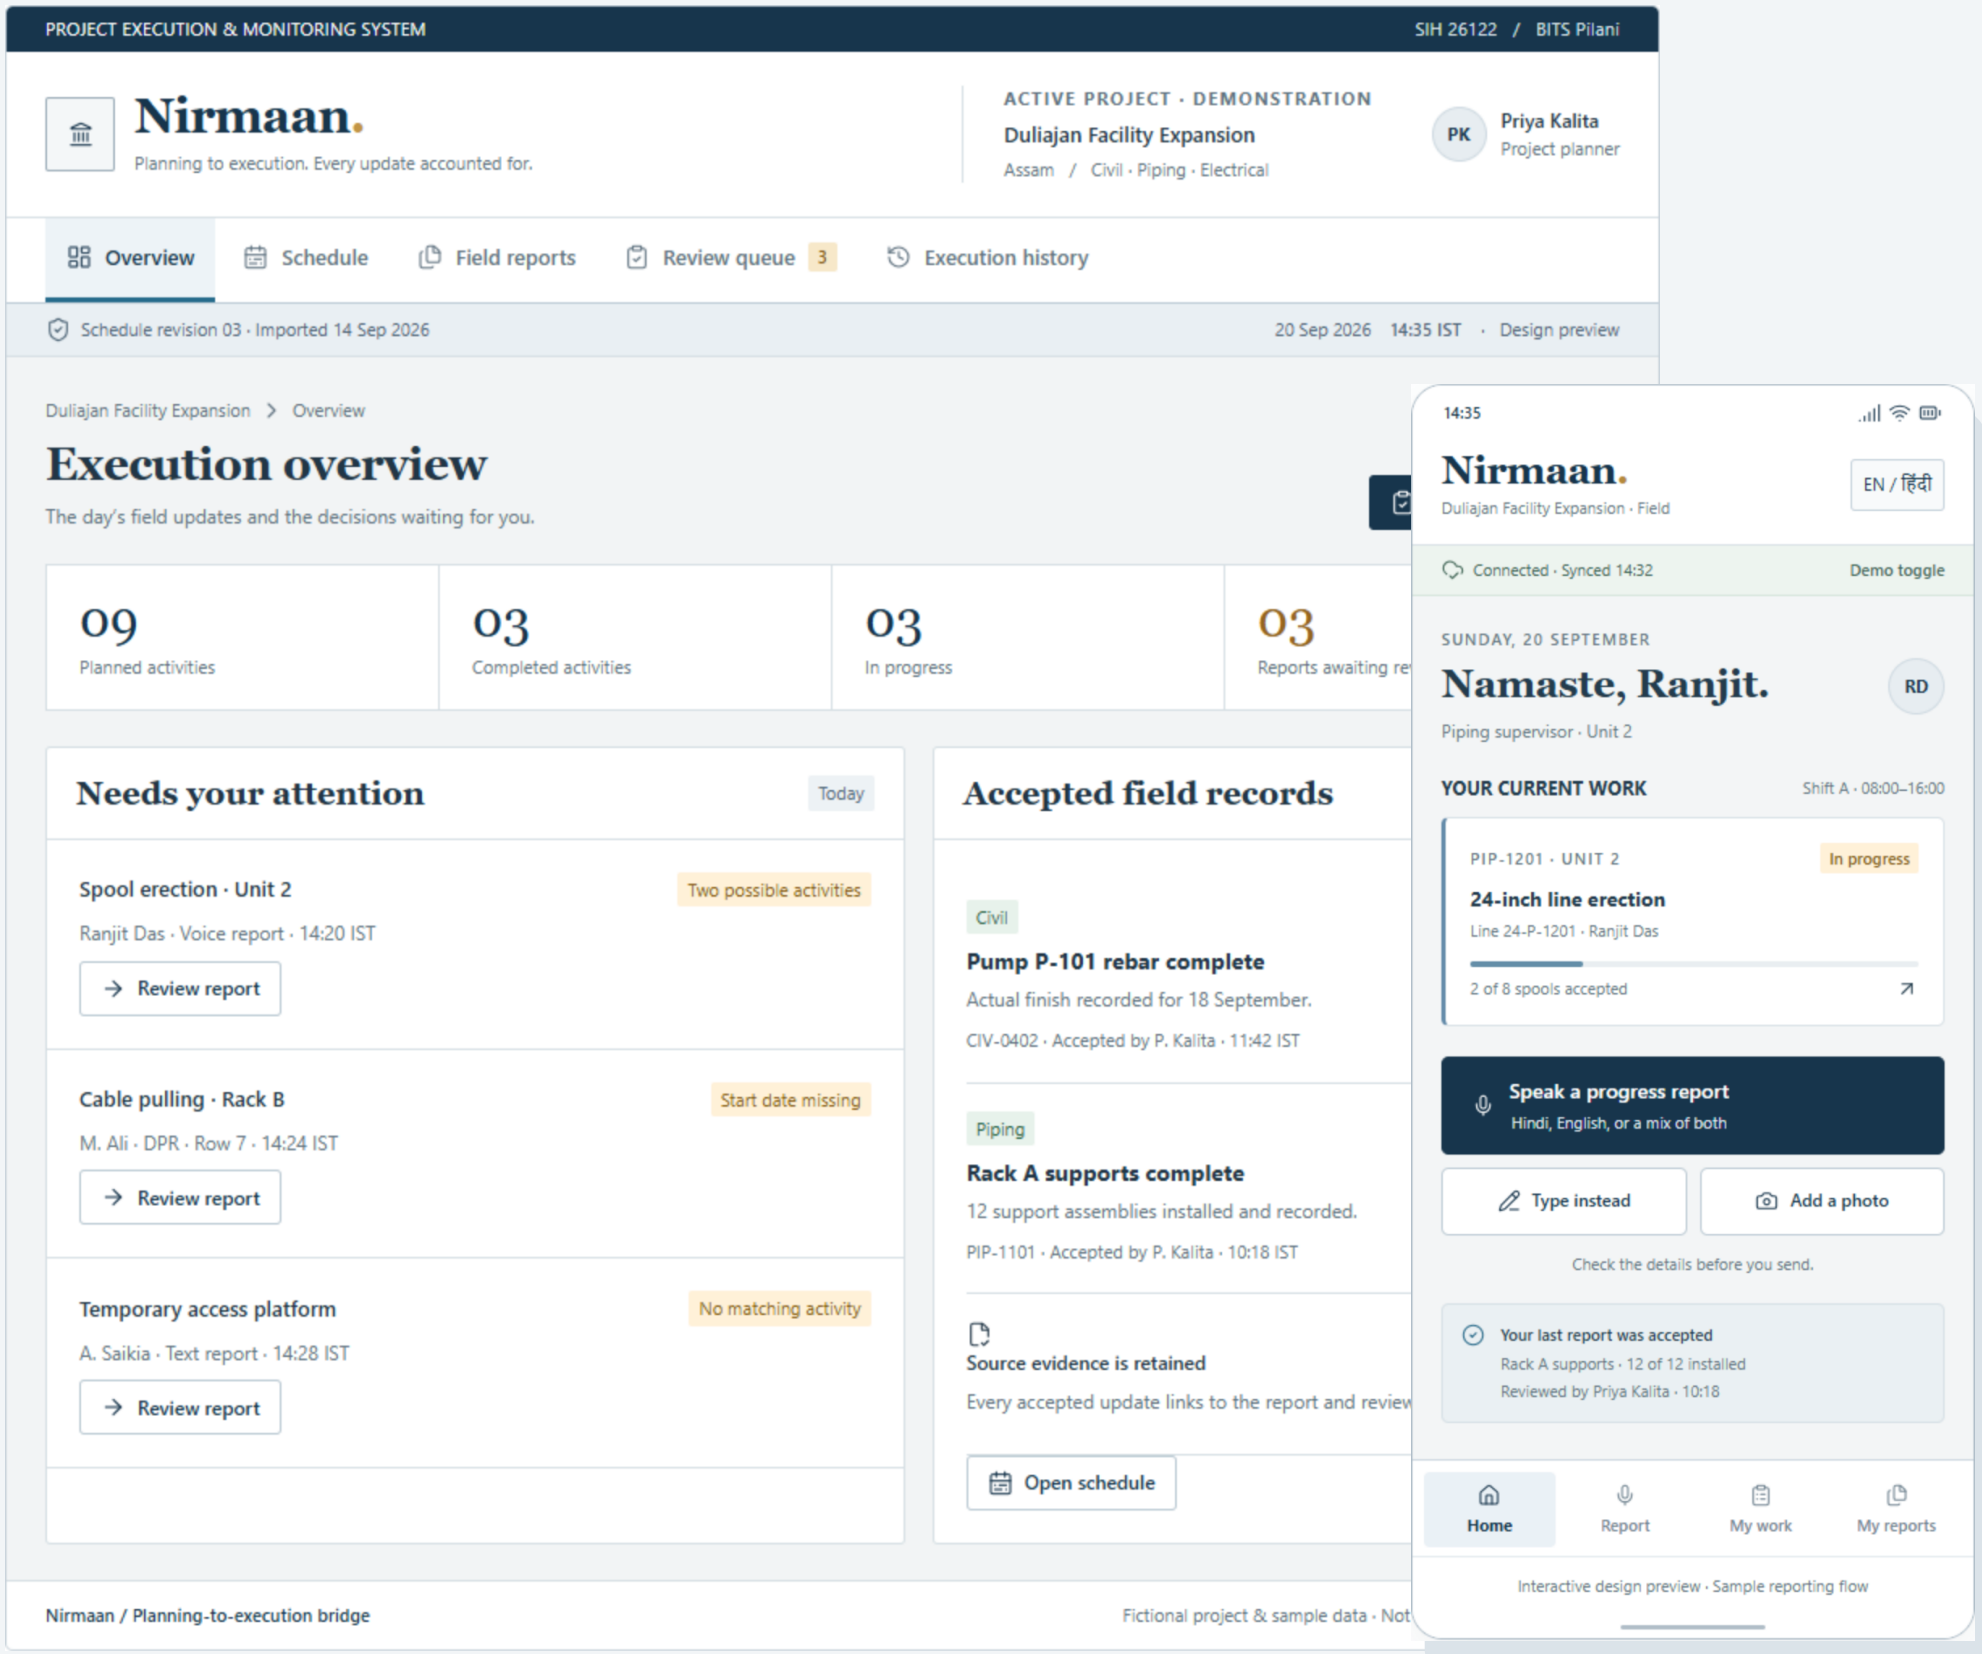


Formal navigation. Clear records. Simple reporting.

Fictional project and sample data. Independent student prototype; not an official Oil India service.

Execution overview

Start with pending decisions, then inspect the accepted record.

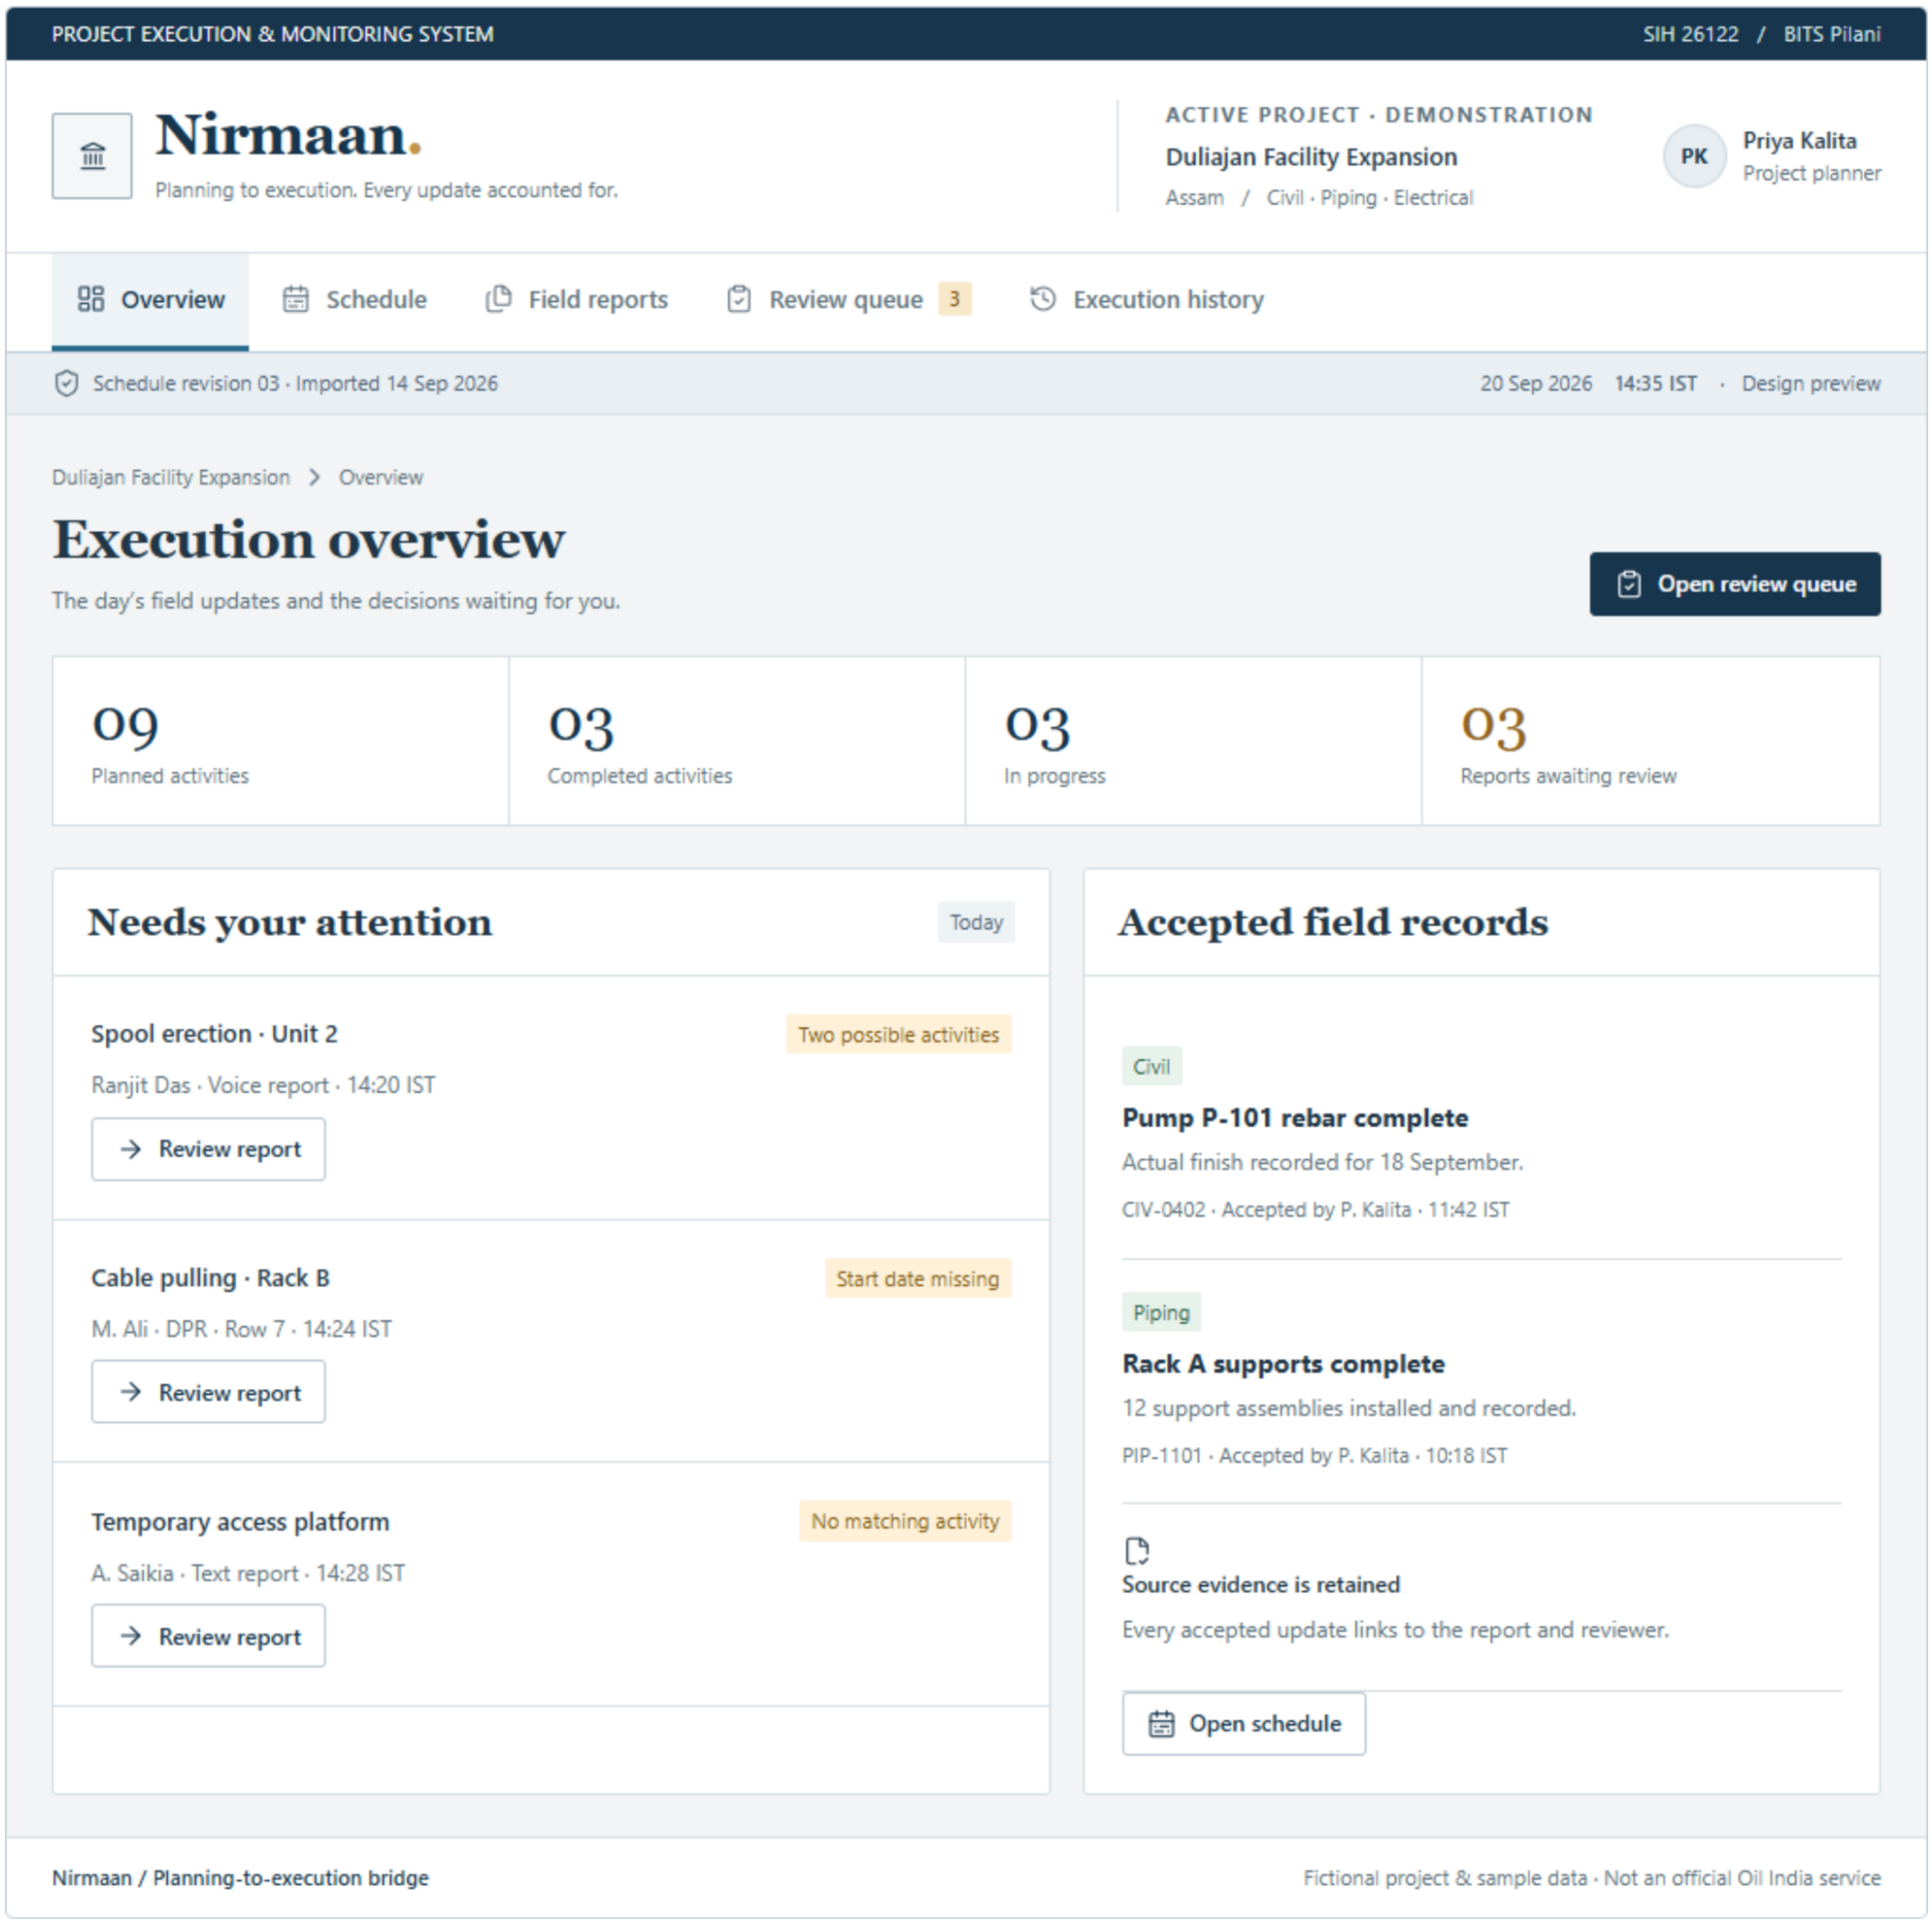

One place to act


The planner sees work awaiting review, the person who reported it and the reason a decision is needed.

Measured language

Activity counts are shown directly. An overall completion percentage needs a defined weighting method.

The project schedule

The original Gantt reference, adapted to a formal horizontal navigation system.

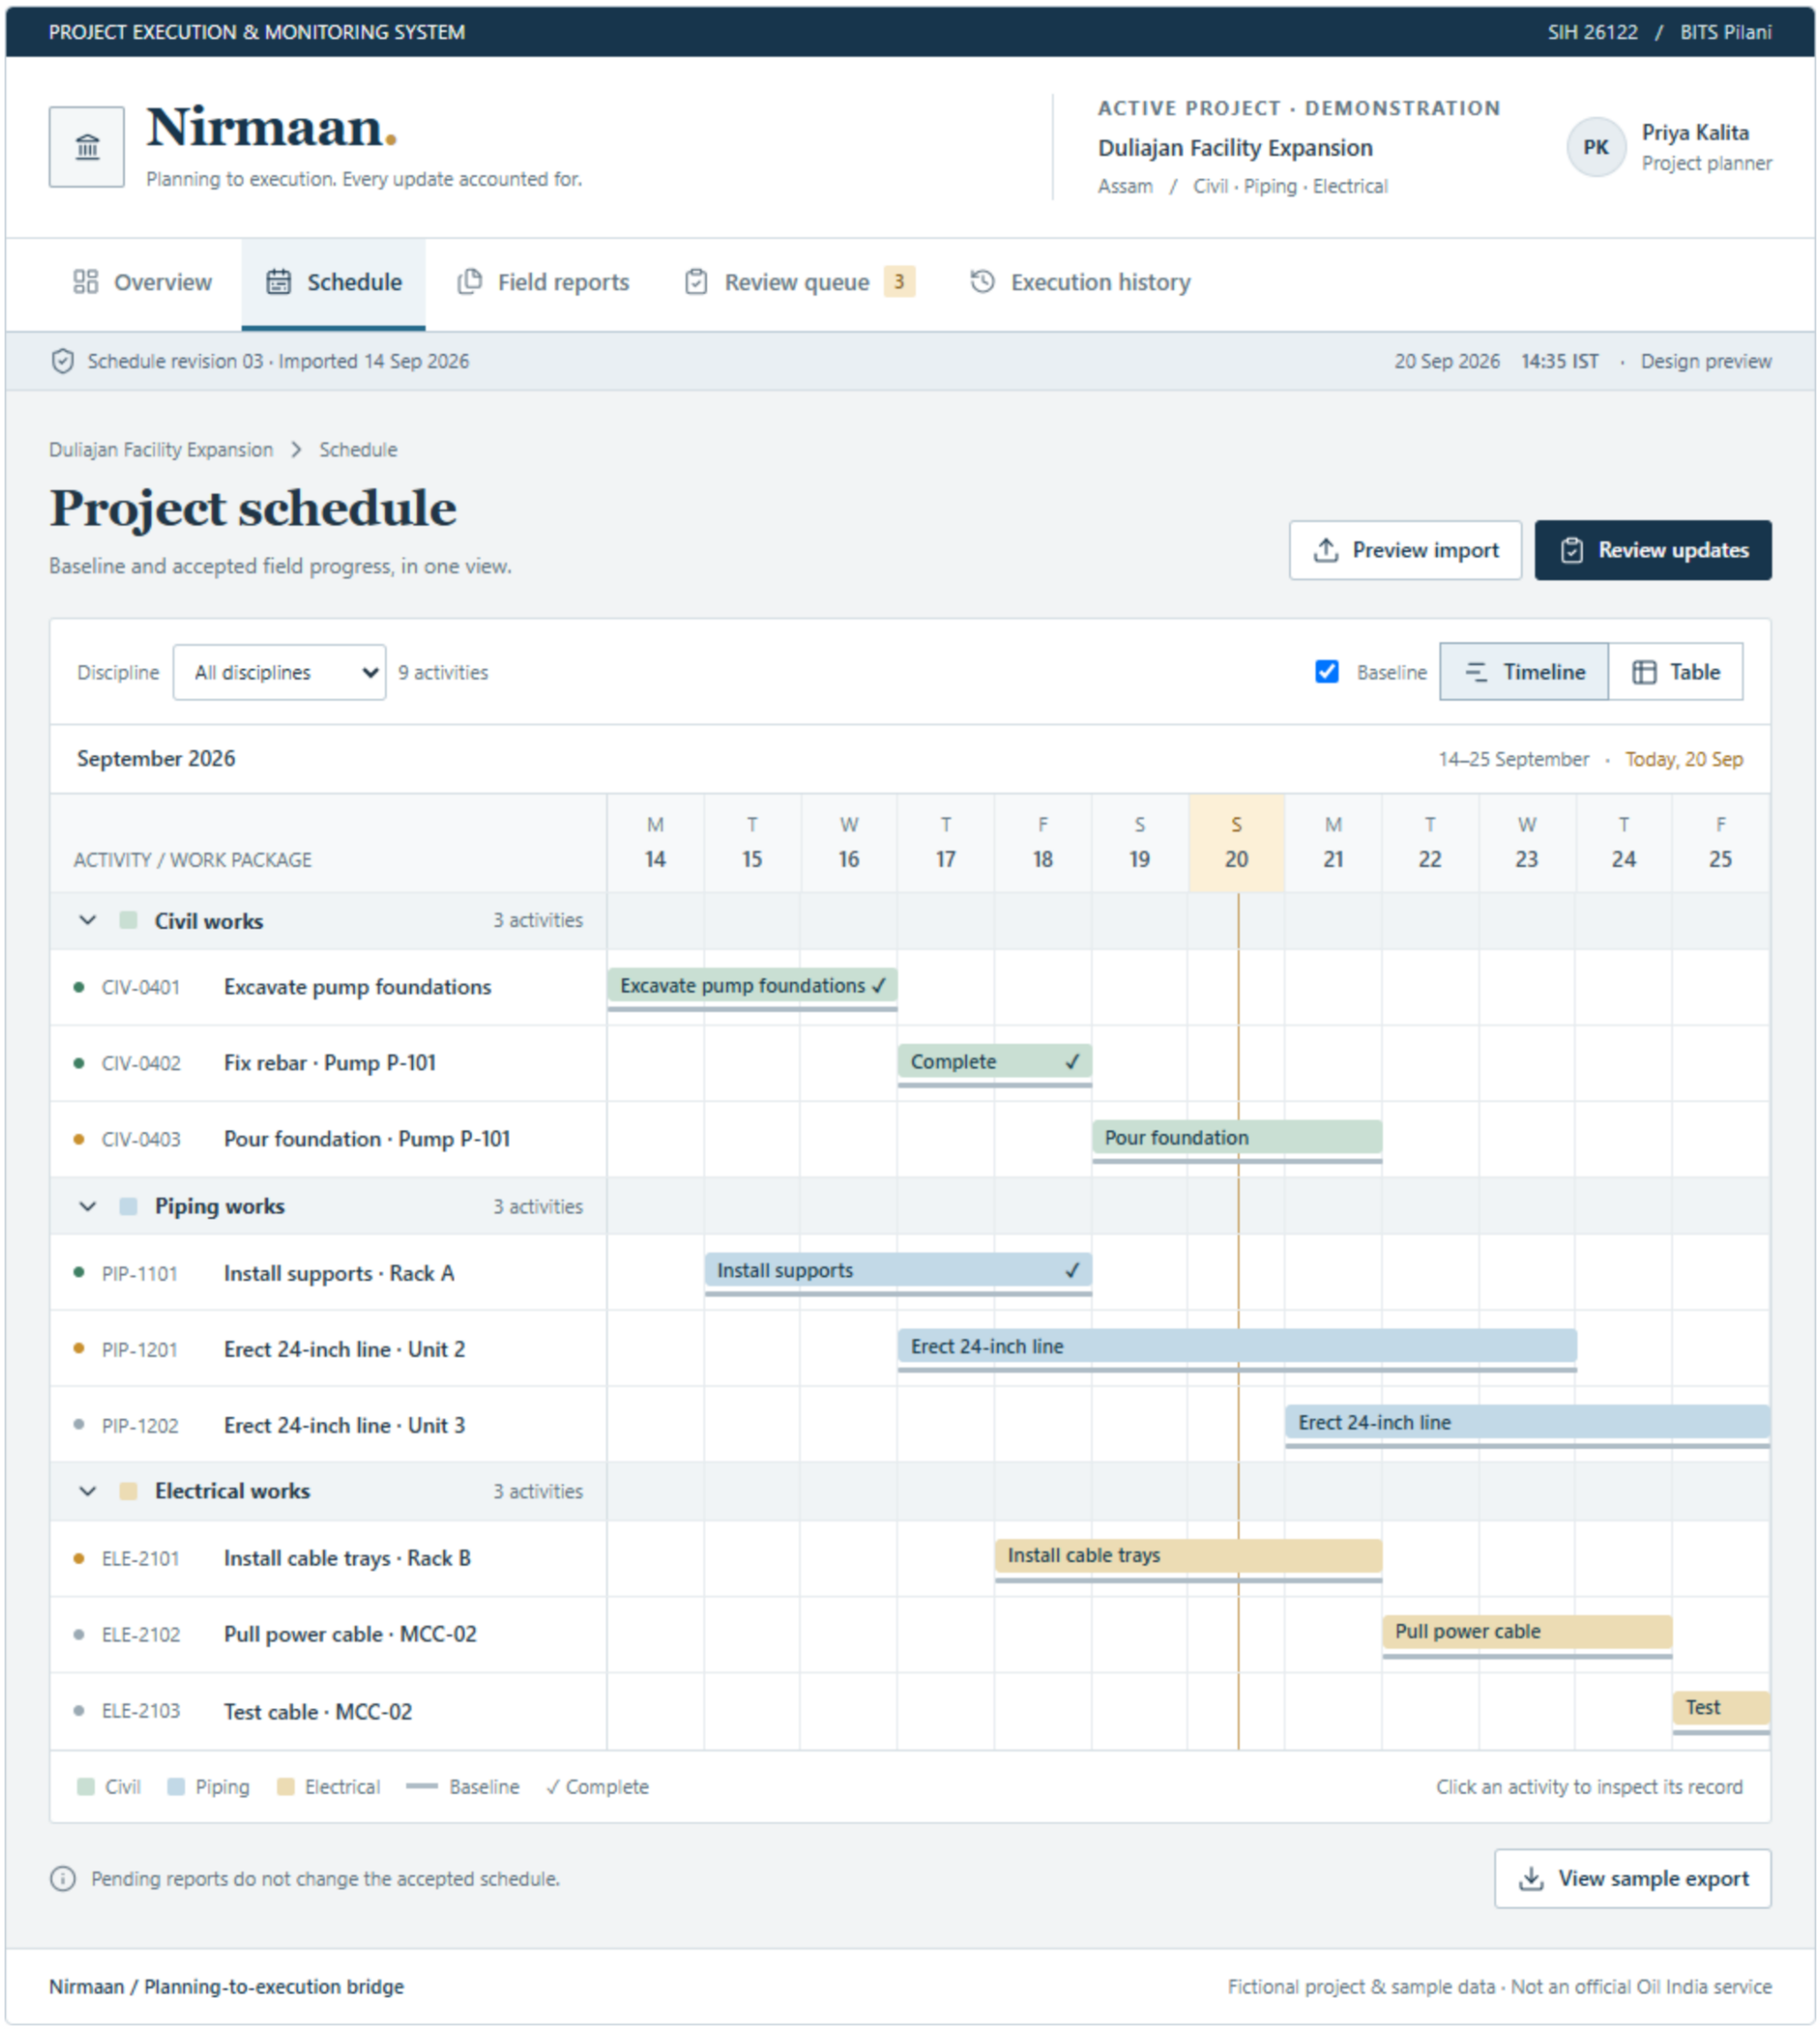

Plan and execution together


Civil, piping and electrical work stay grouped. A table view, discipline filter and baseline toggle support daily checks.

Review stays separate

Pending field reports do not automatically modify accepted actuals. The demonstration timeline is a fixed sample.

An inspectable activity record

Open an activity without losing the context of the schedule.

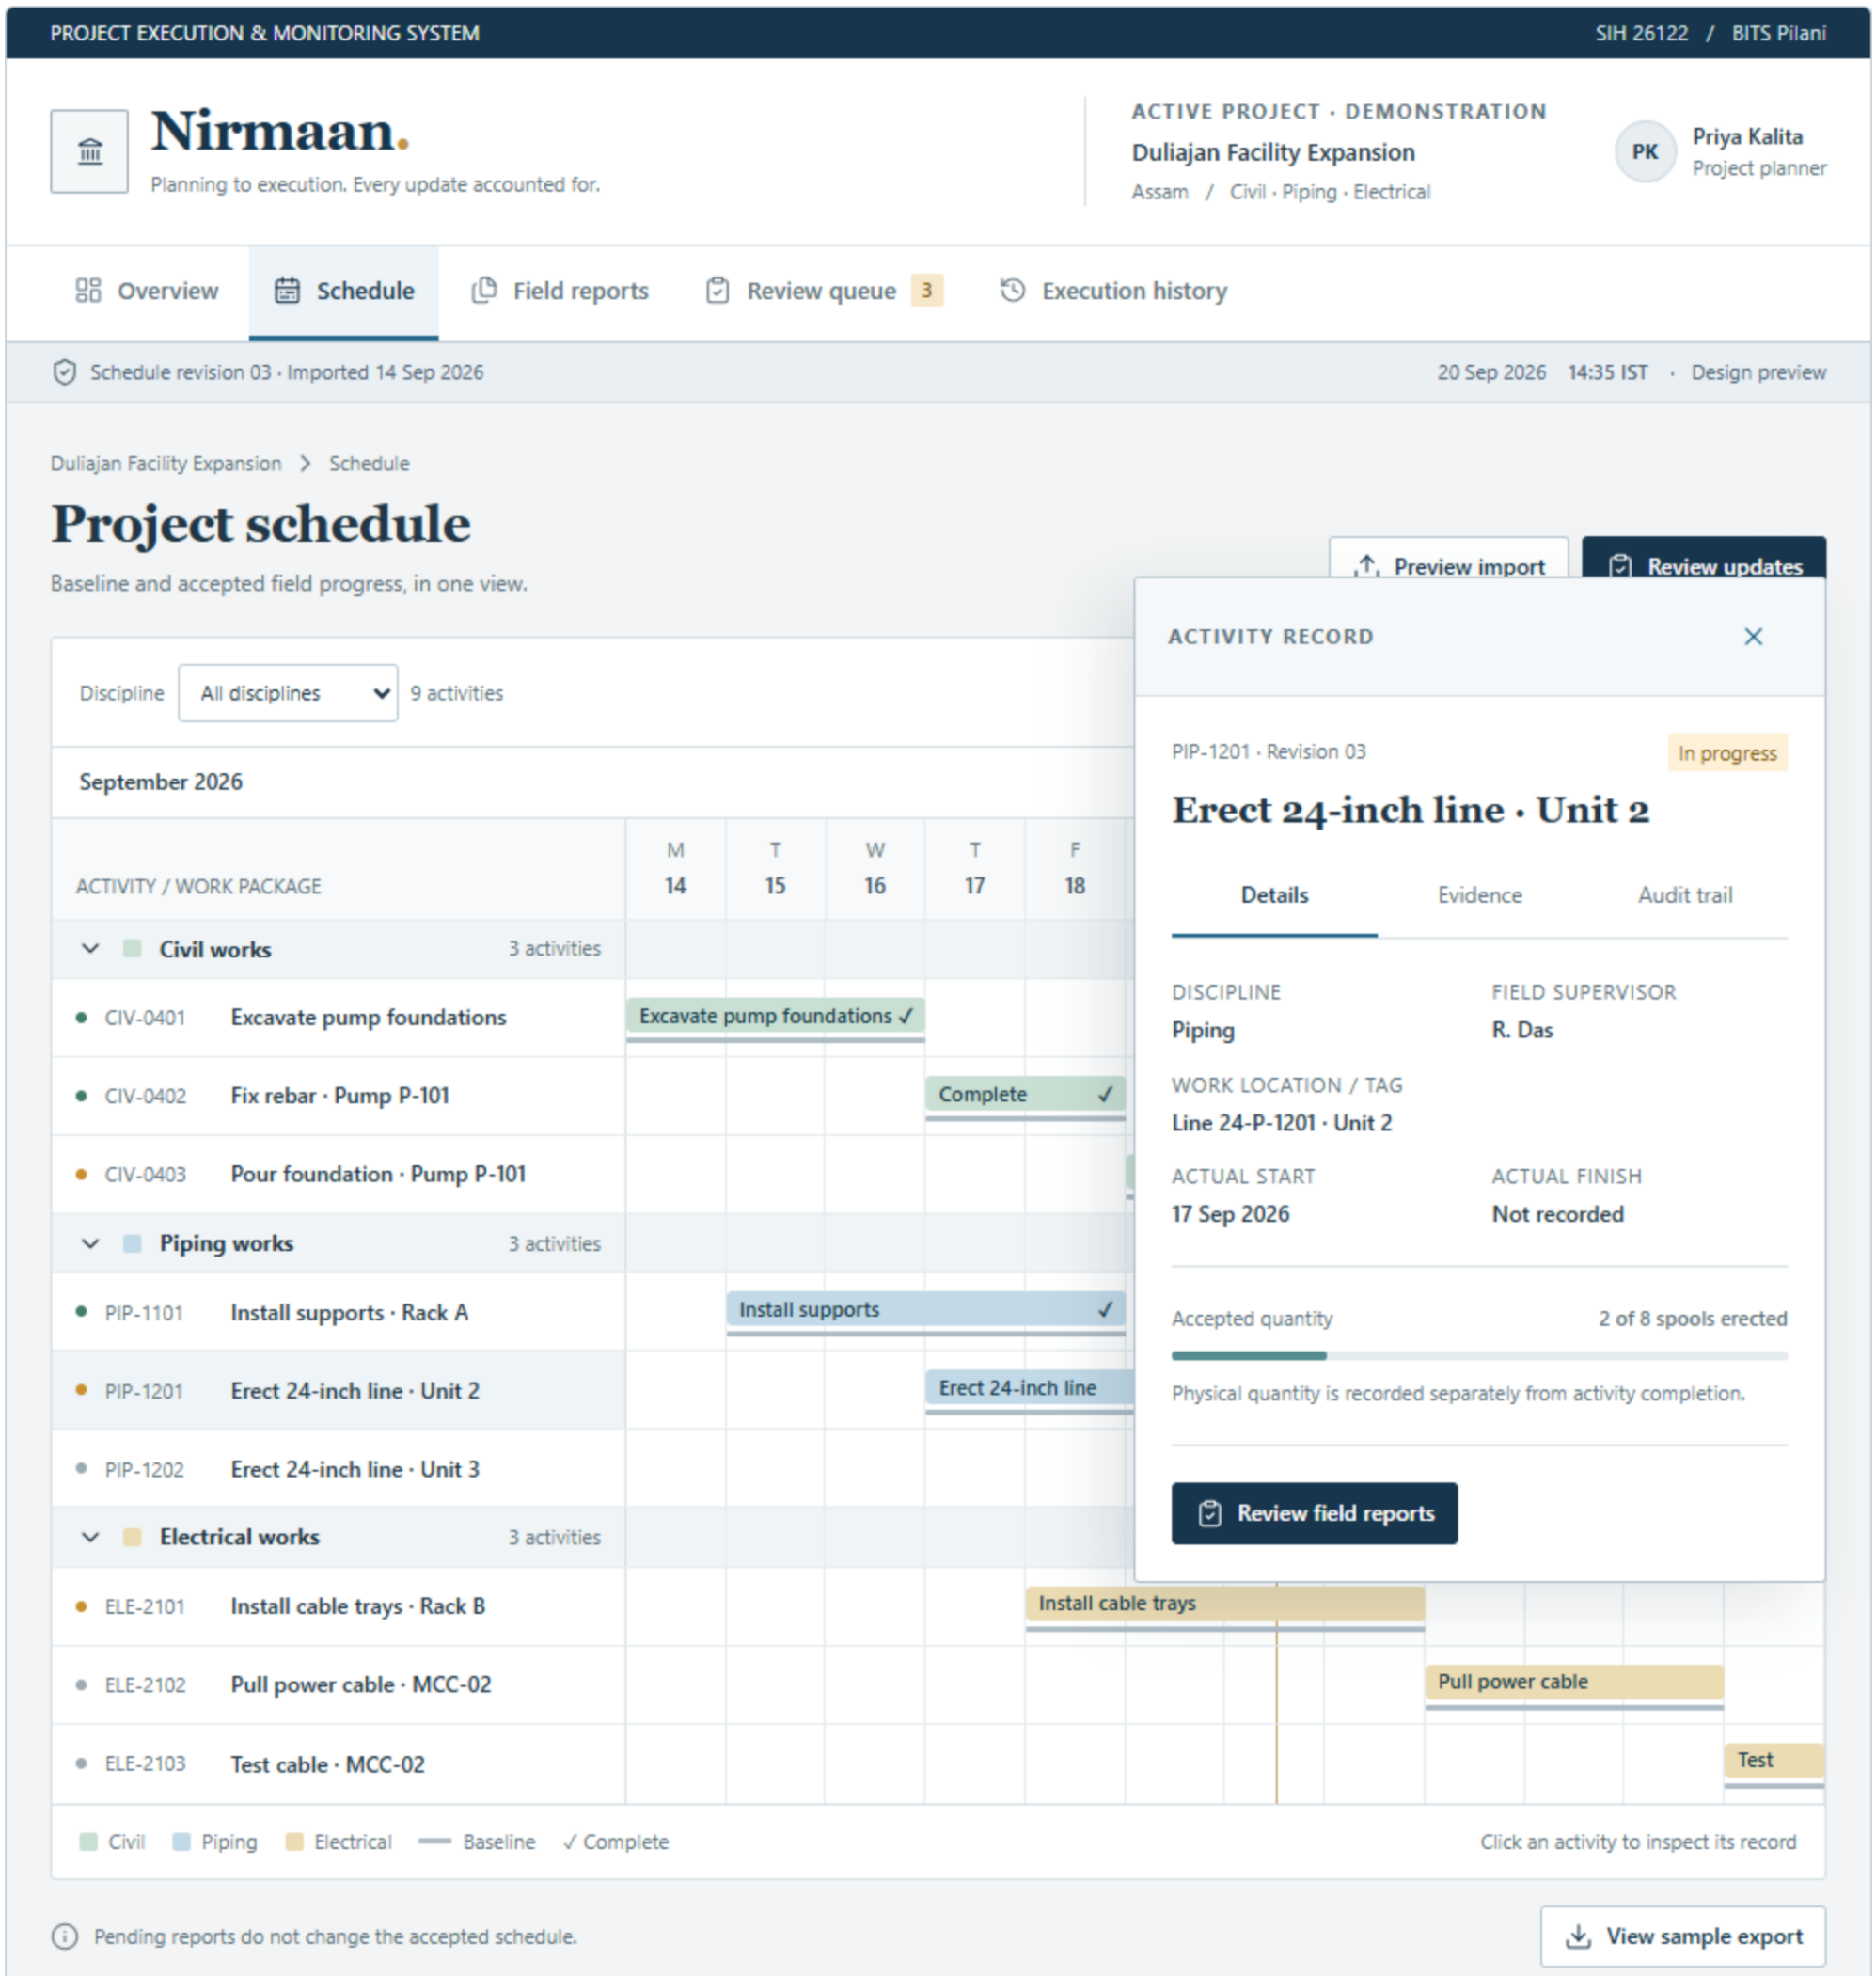

Details, evidence and audit


The side panel keeps the activity ID, field supervisor, location, actual dates and source history close together.

Quantity is not completion

Two erected spools do not mean the whole line is finished. An unknown actual finish remains visibly unrecorded.

Review before acceptance

Read the original report, check the proposed activity and resolve uncertainty.

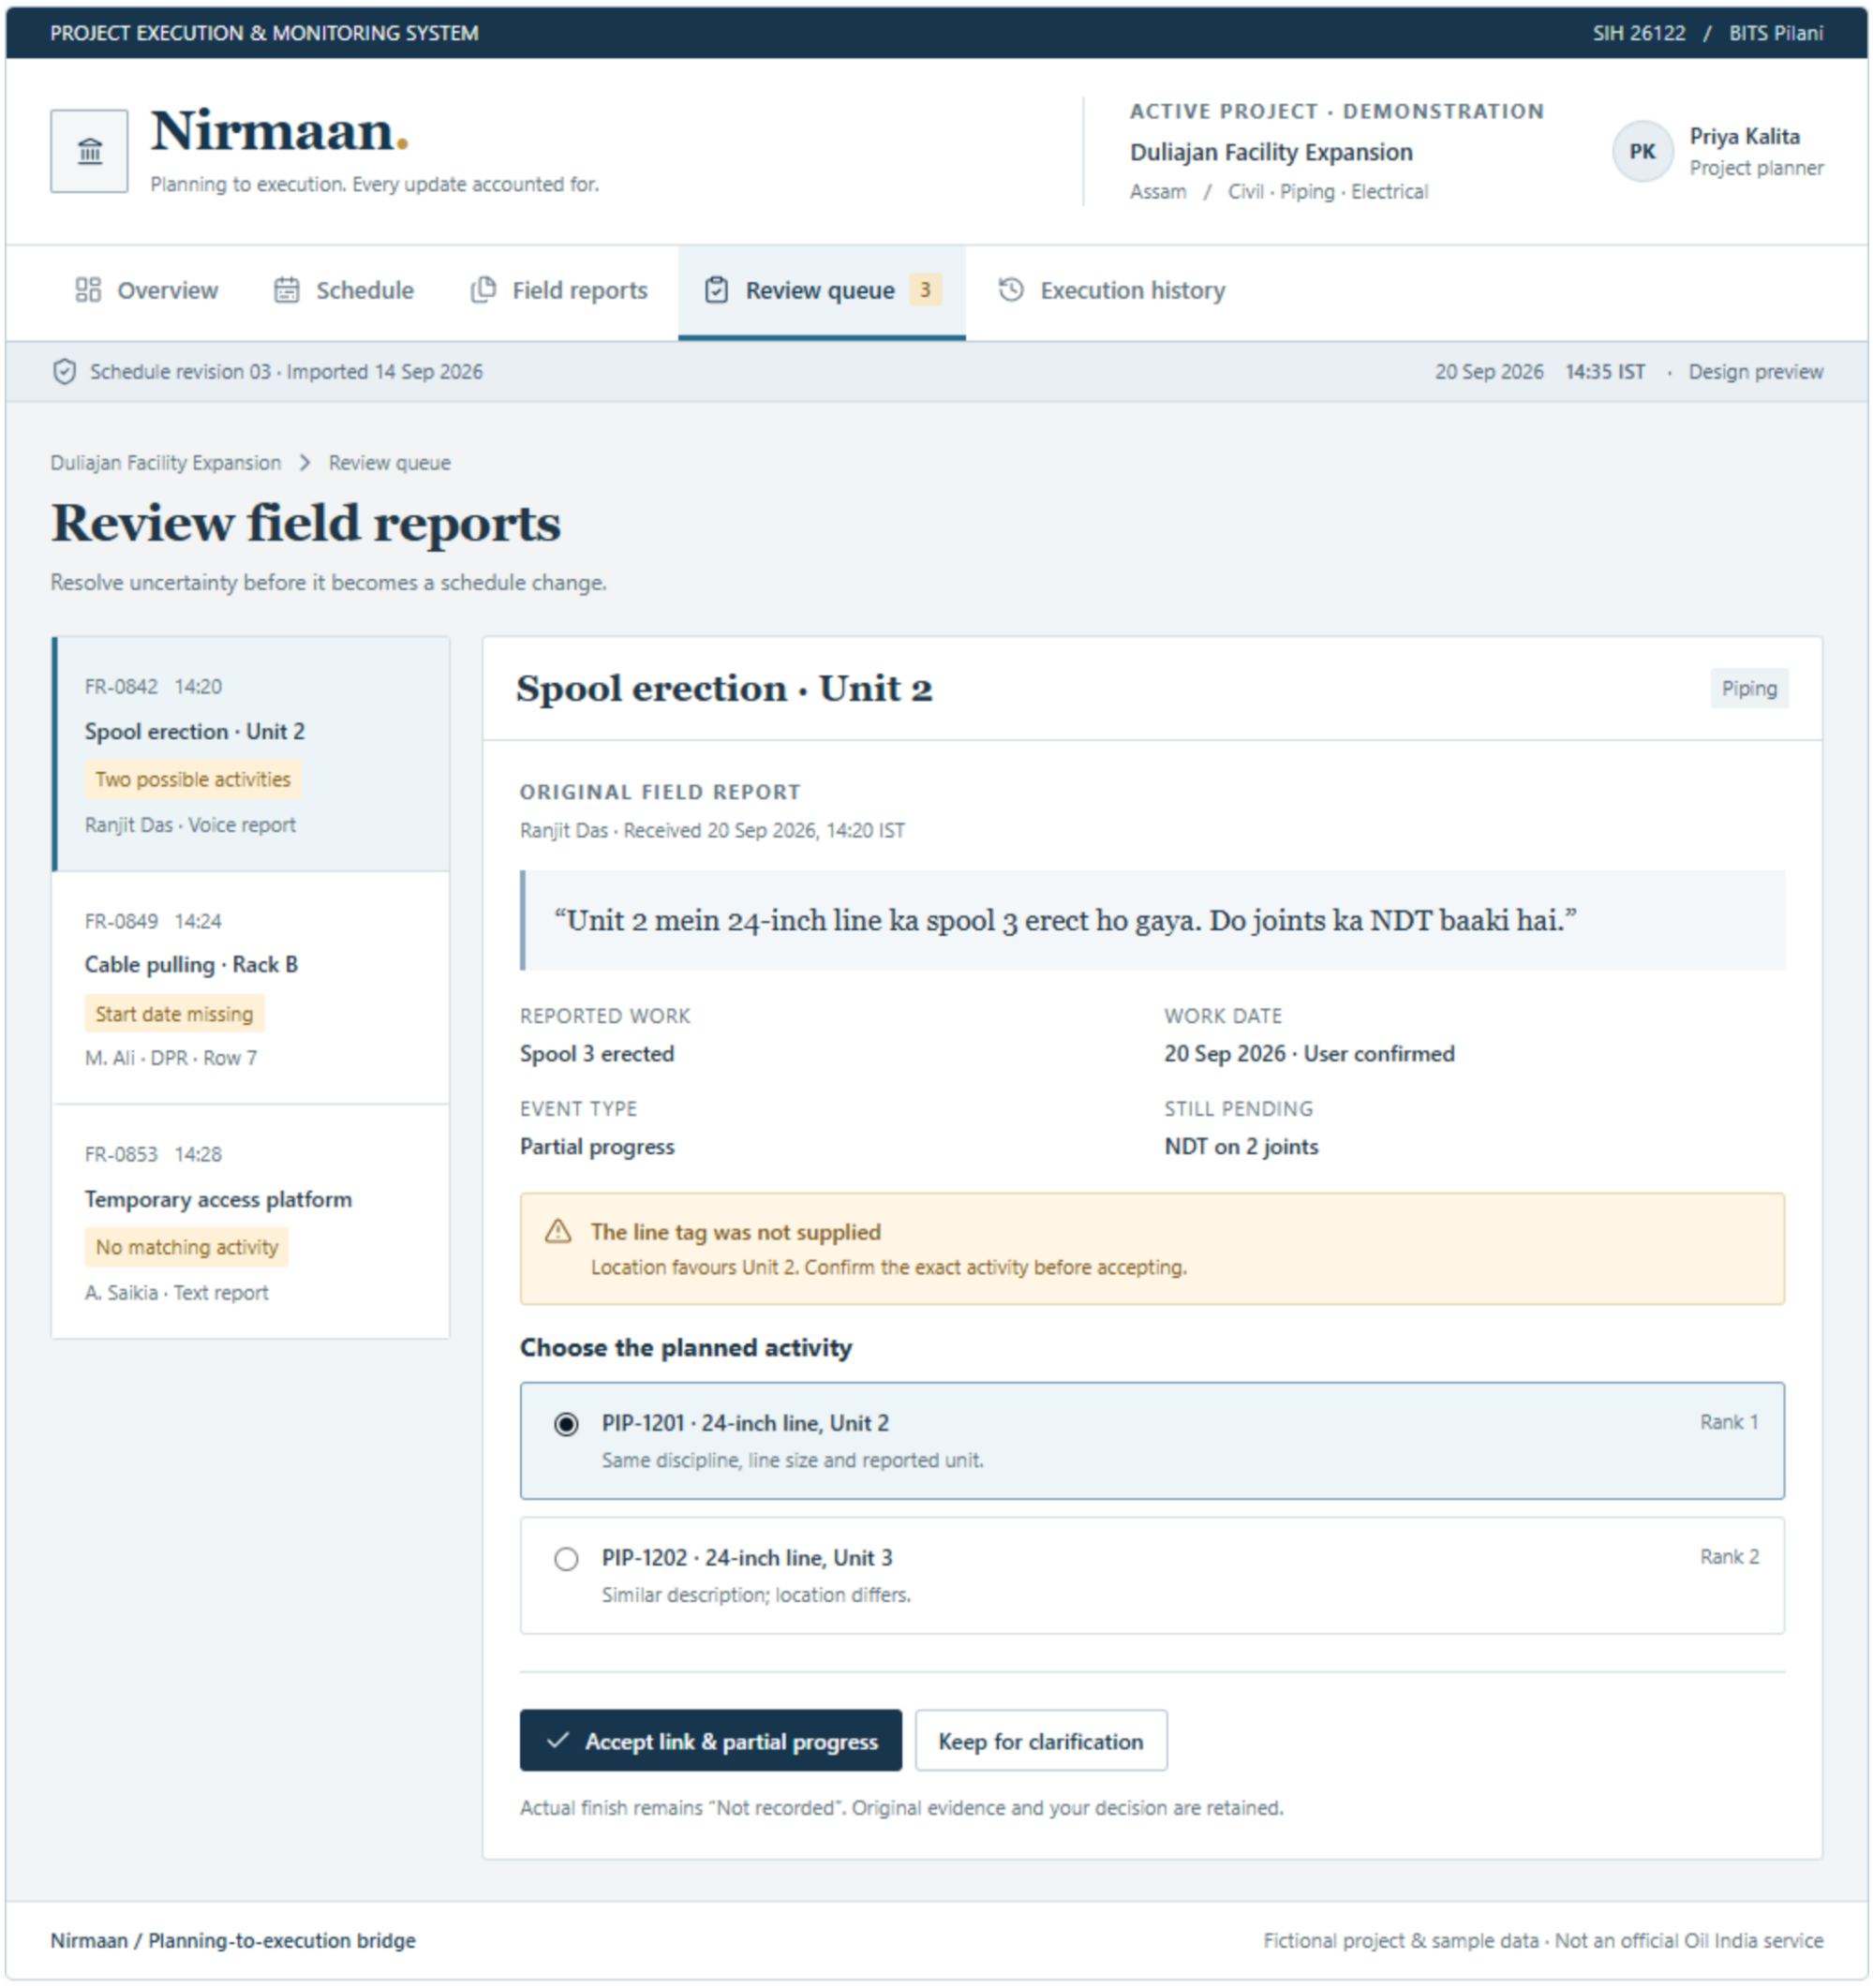

Explain the match


A missing line tag creates a review task. Candidate descriptions and their locations make the choice inspectable.

Preserve the qualification

The sample reports spool erection with NDT still pending. Accepting the link records partial work, not a finished line.

The field reporting register

Keep voice, text and daily progress report entries in a single accountable record.

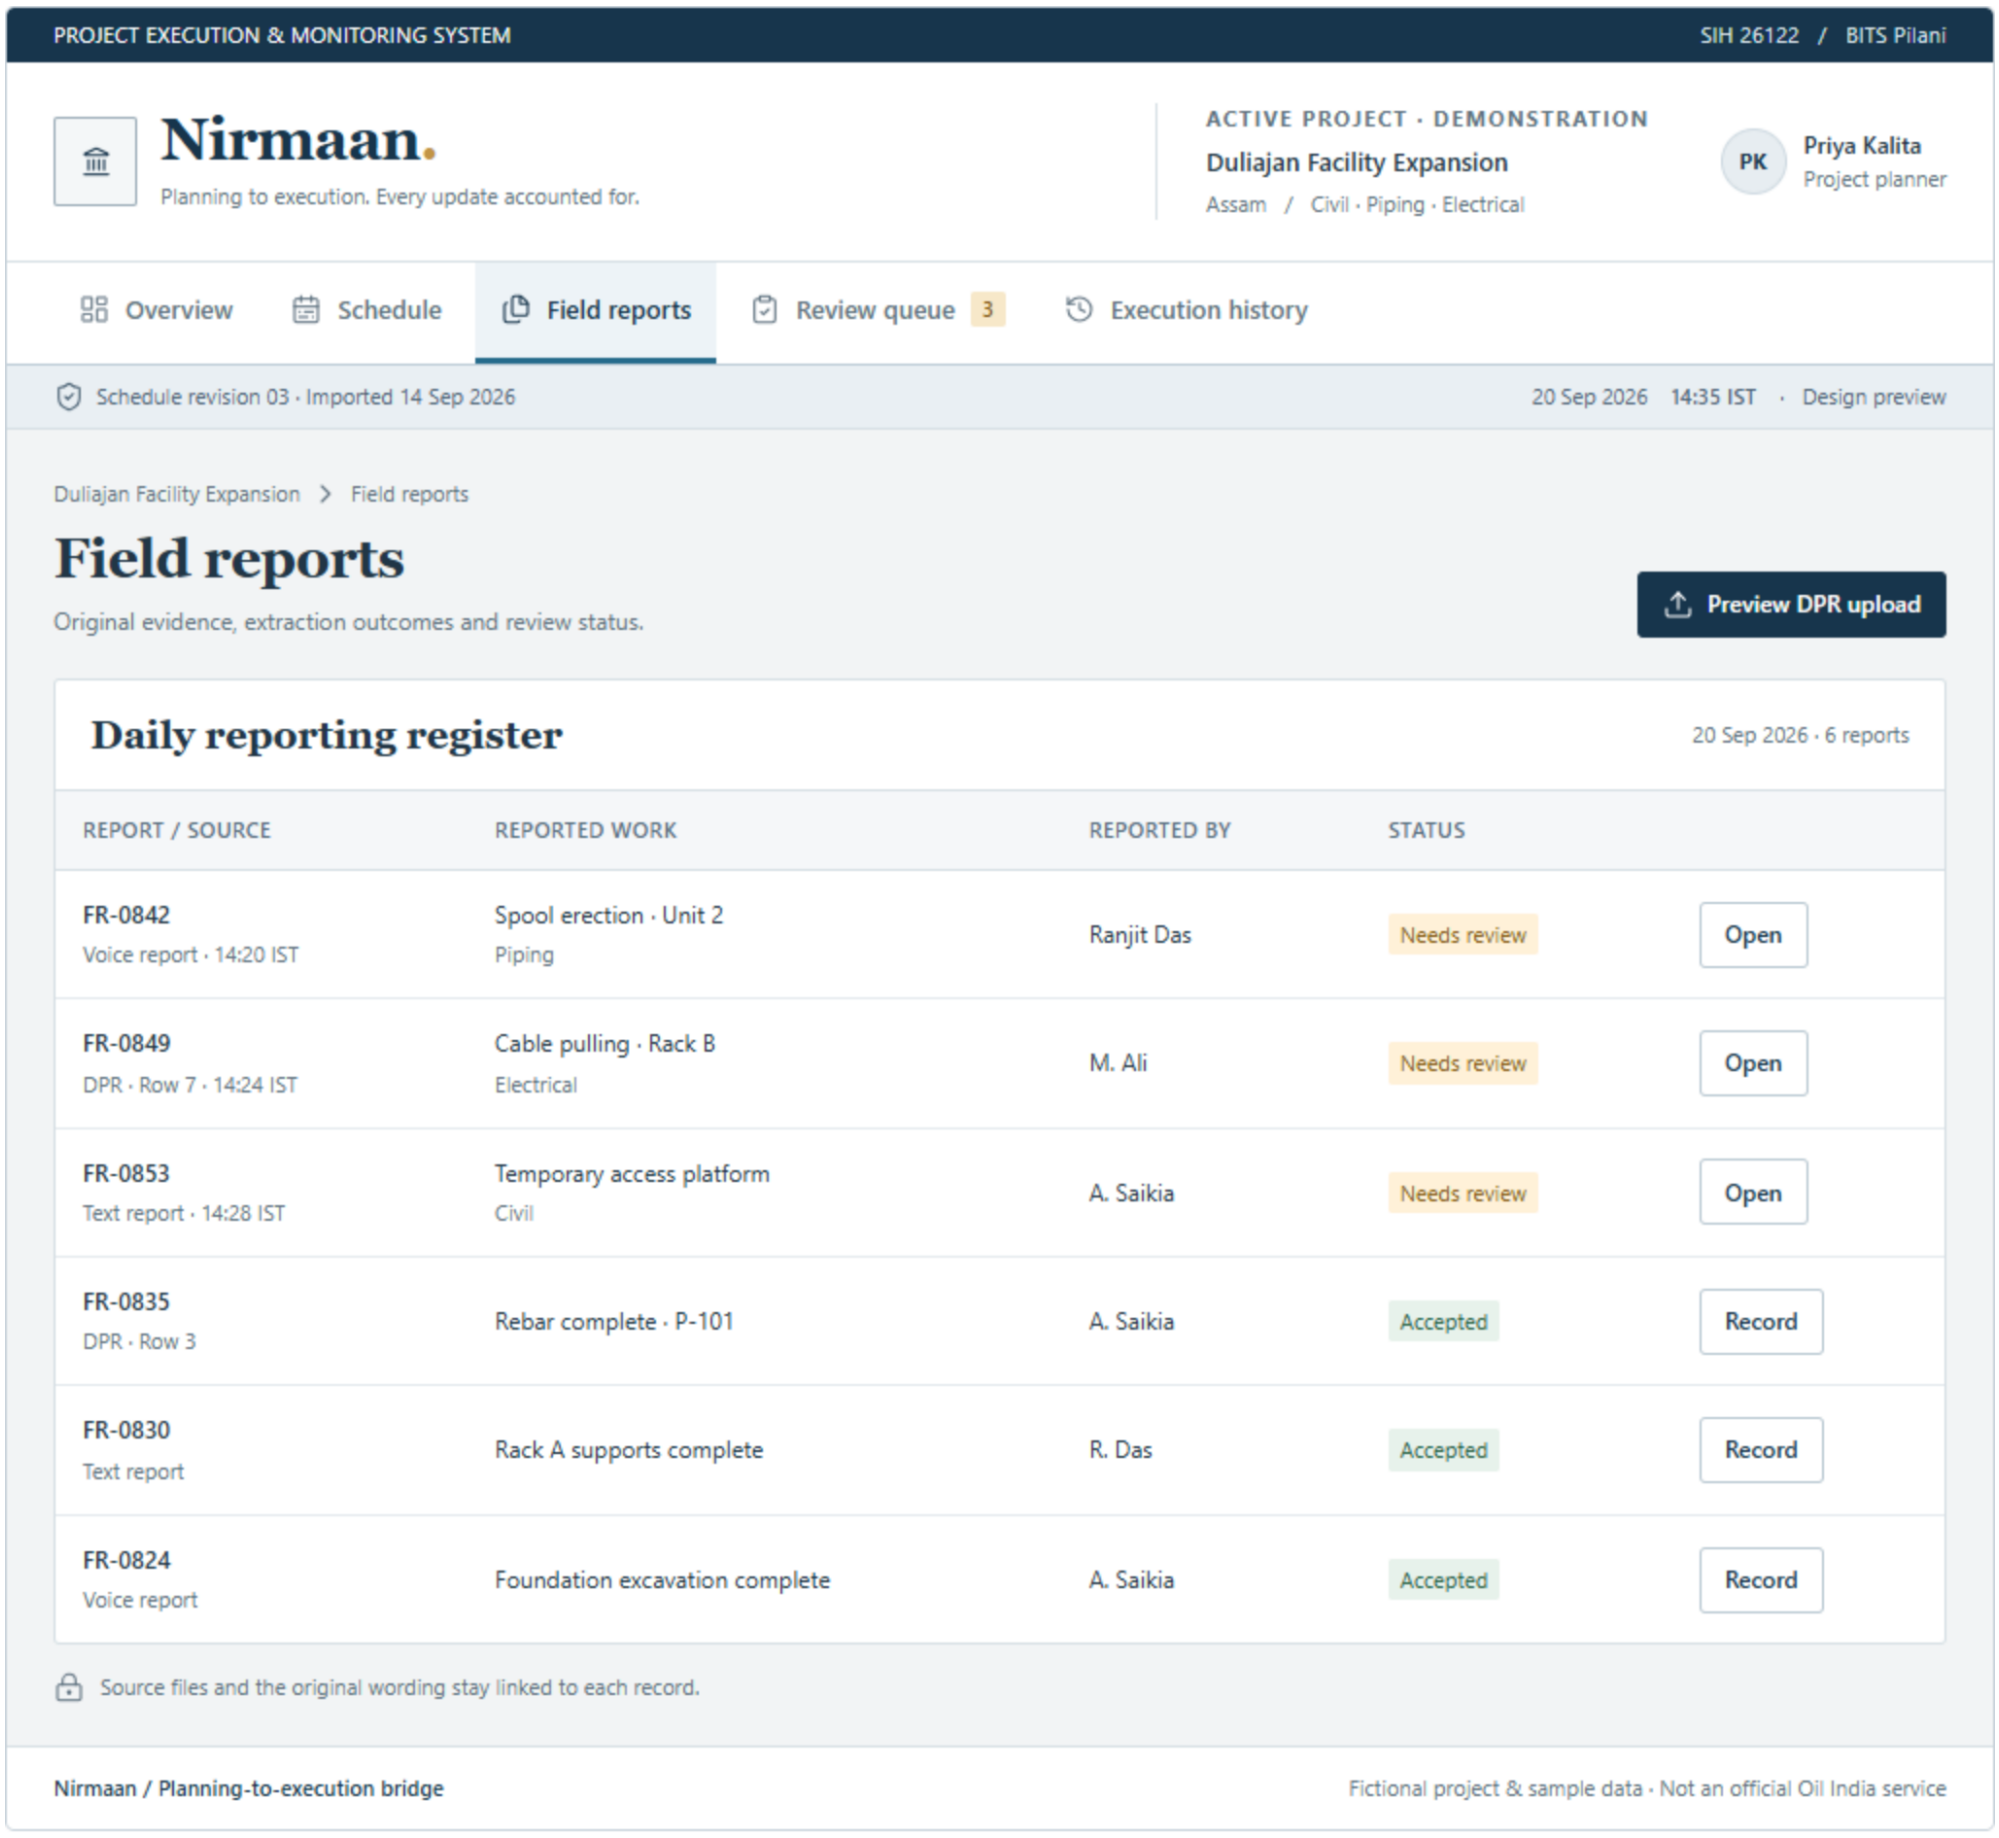

Every report stays visible


Each entry retains its source type, reporter and review state, including reports that cannot yet be safely linked.

Handle different input formats

The sample DPR import preview shows column mapping and routes a row with a missing work date to the review queue.

Execution history

Build institutional memory from accepted activity records and verified terminology.

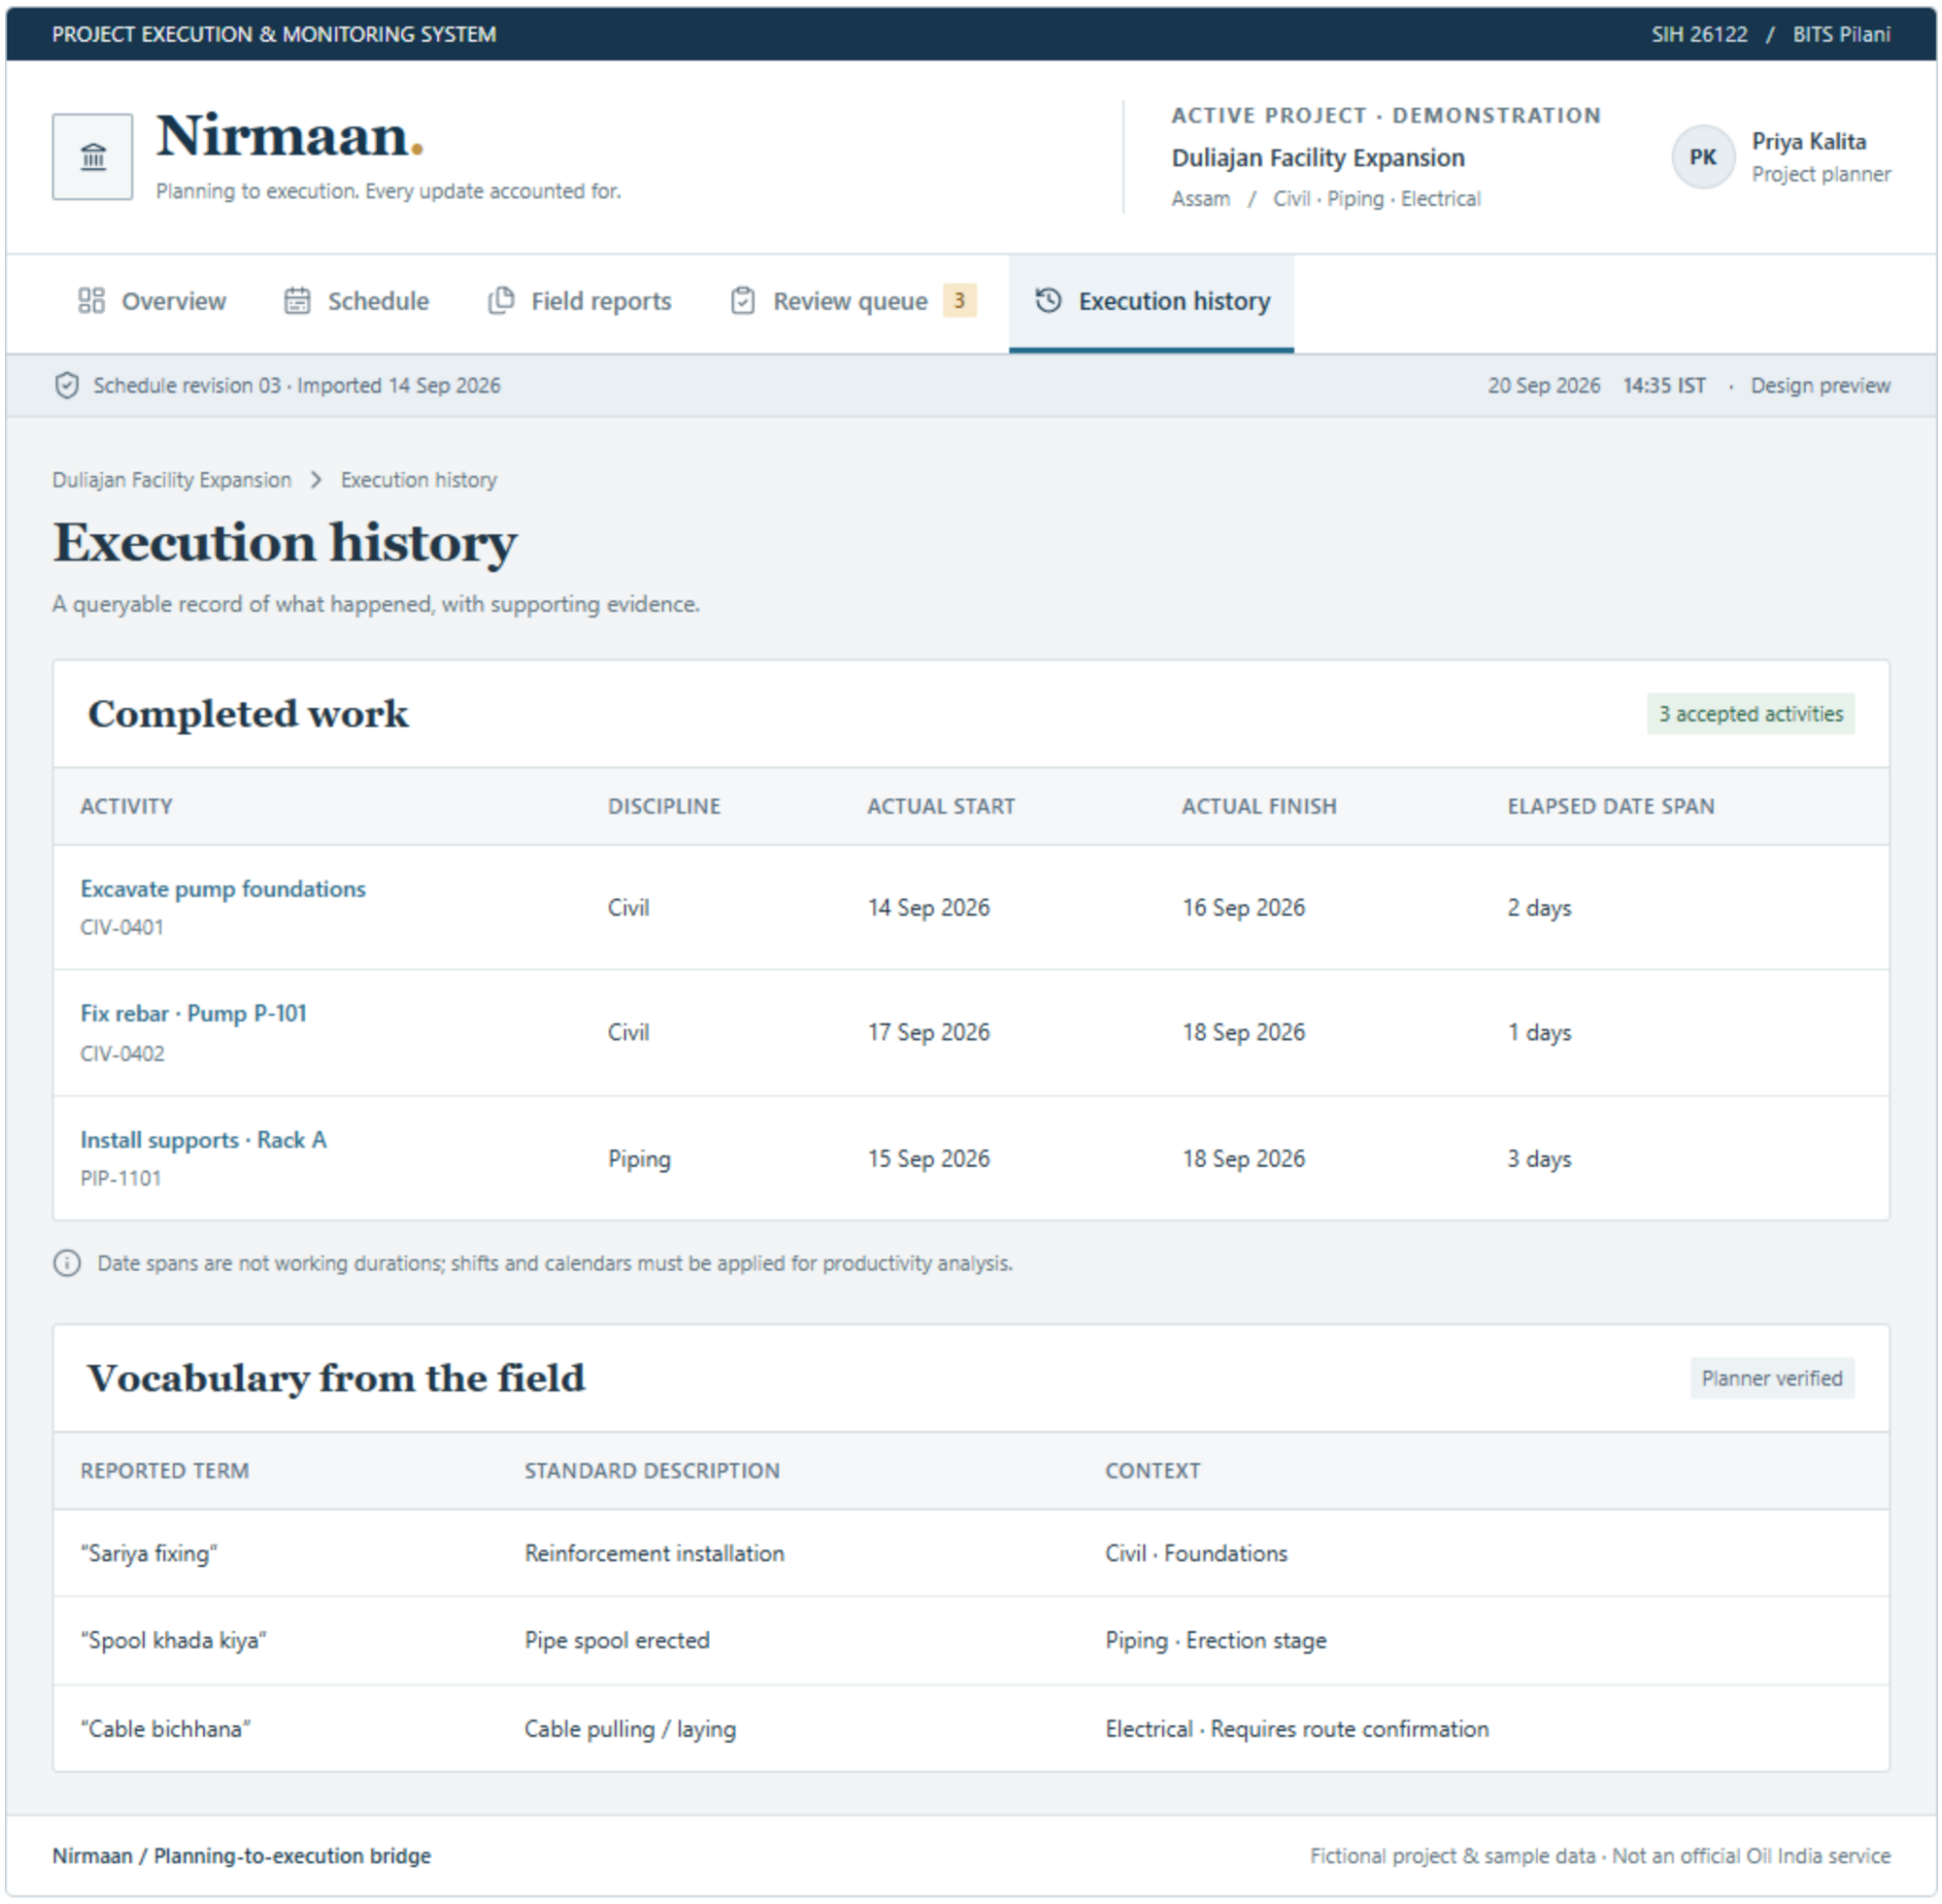

Start from evidence

Completed activities retain their actual dates and IDs so a planner can return to the supporting record.


Avoid misleading analysis

Elapsed date spans are not working durations. Productivity measures need calendars, shifts and a clear quantity basis.


Field work, made immediately clear

Show the current assignment and put reporting within easy reach.

01 Home and current work

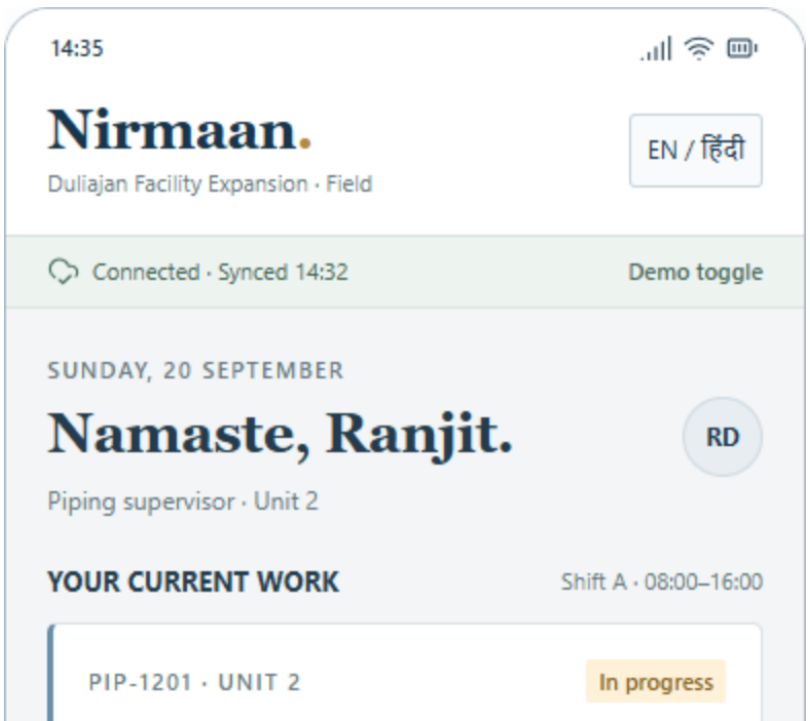

02 Assigned activities

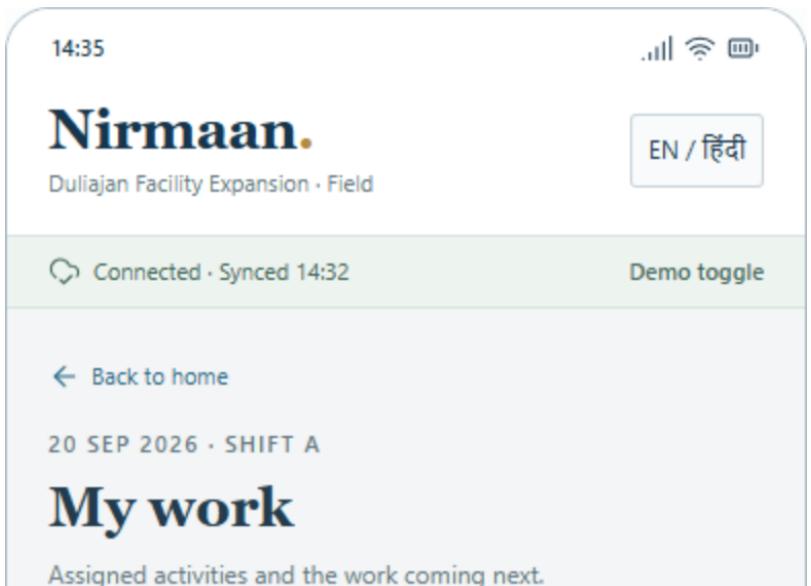

Large, direct controls

Voice, text and photo entry points remain visible. The current work card shows accepted quantity rather than an unexplained score.


A simpler field view

The worker sees today’s assignment and the next activity. Detailed schedule controls remain with the planner.

Speak, then check

The report is editable and reviewable before it reaches the planner.

01 Voice reporting

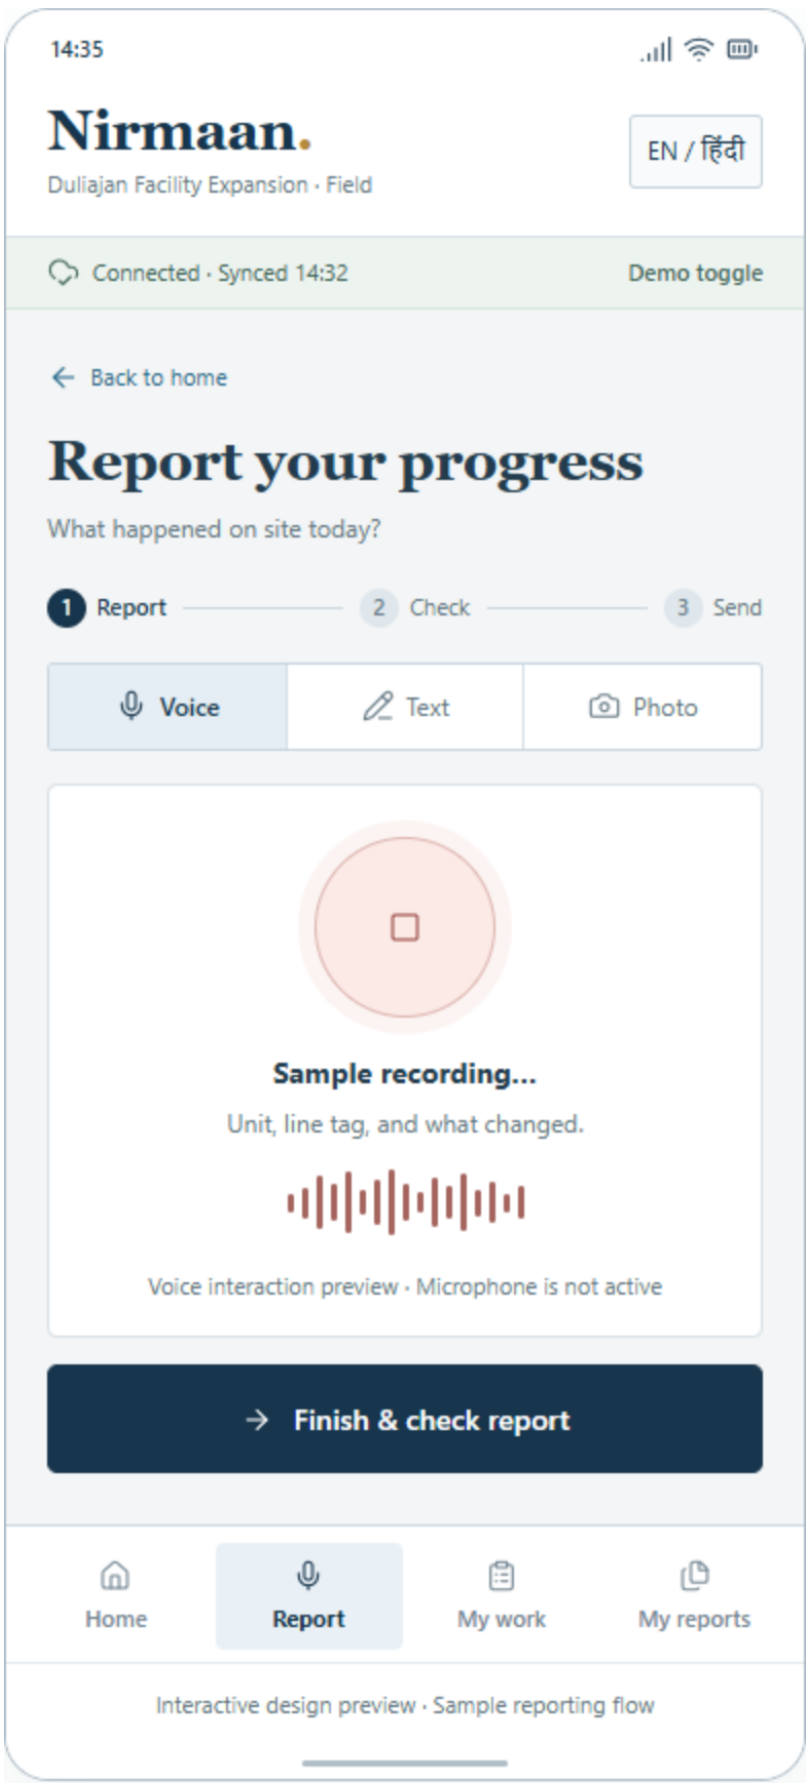

02 Confirmation



Keep reporting natural

The interface is designed for Hindi, English and mixed speech. This preview uses a sample transcript; the microphone is not active.


Make the meaning visible

Show the words, work date and suggested activity. Explicitly retain unfinished work, such as the two joints awaiting NDT.


A clear delivery state

Saved on a device, sent for review and accepted are different outcomes.

01 Saved while offline

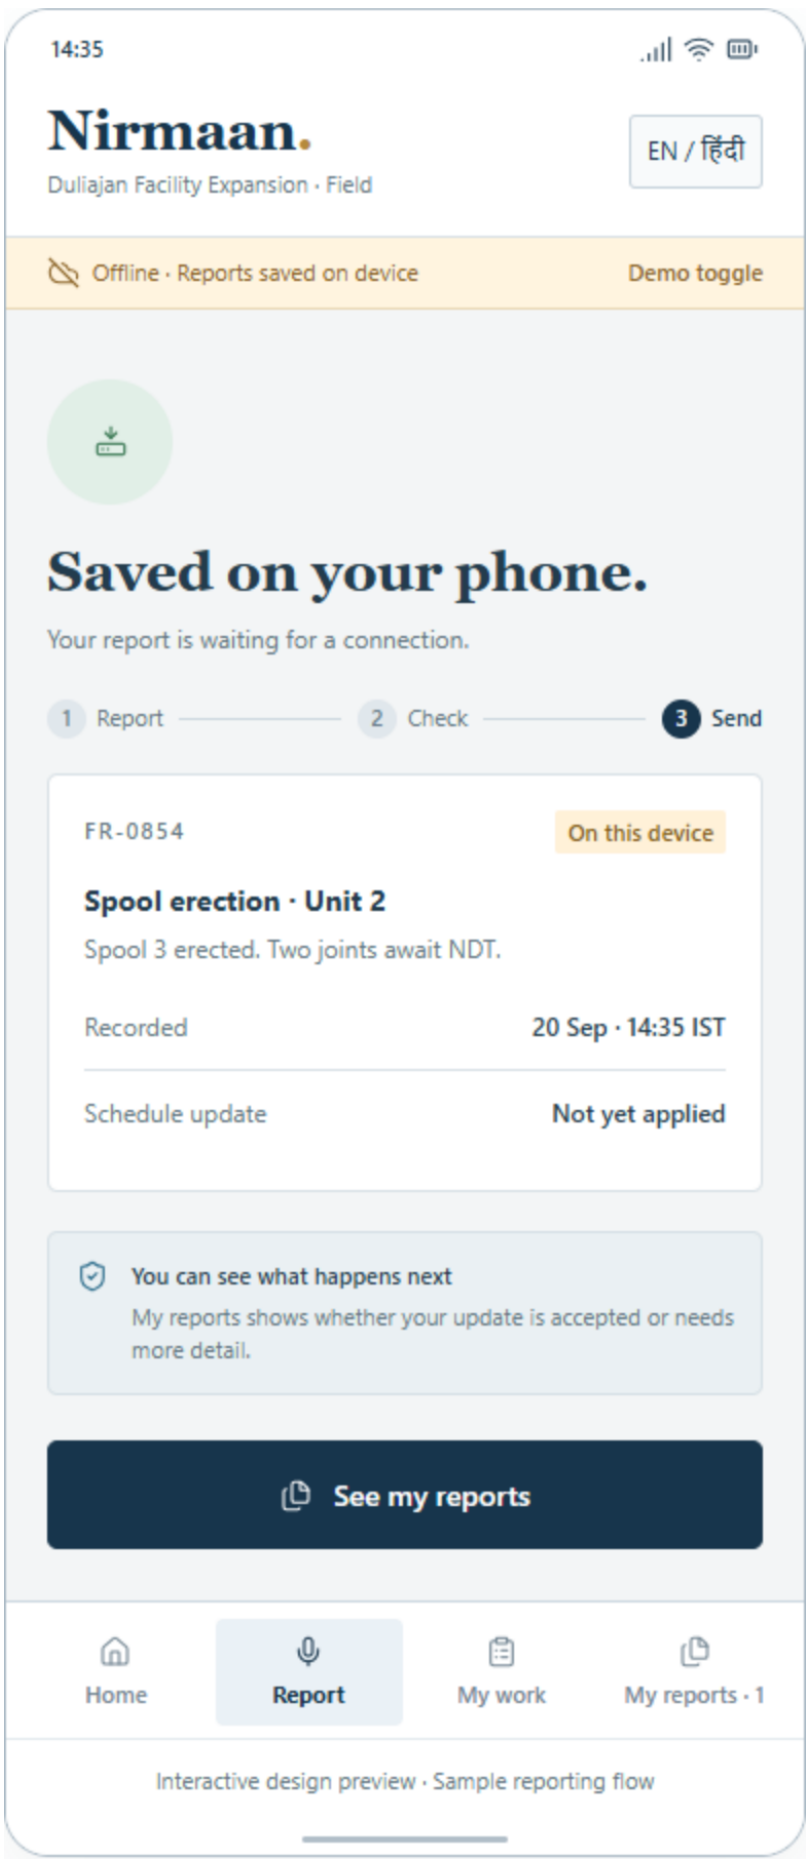

02 After reconnection

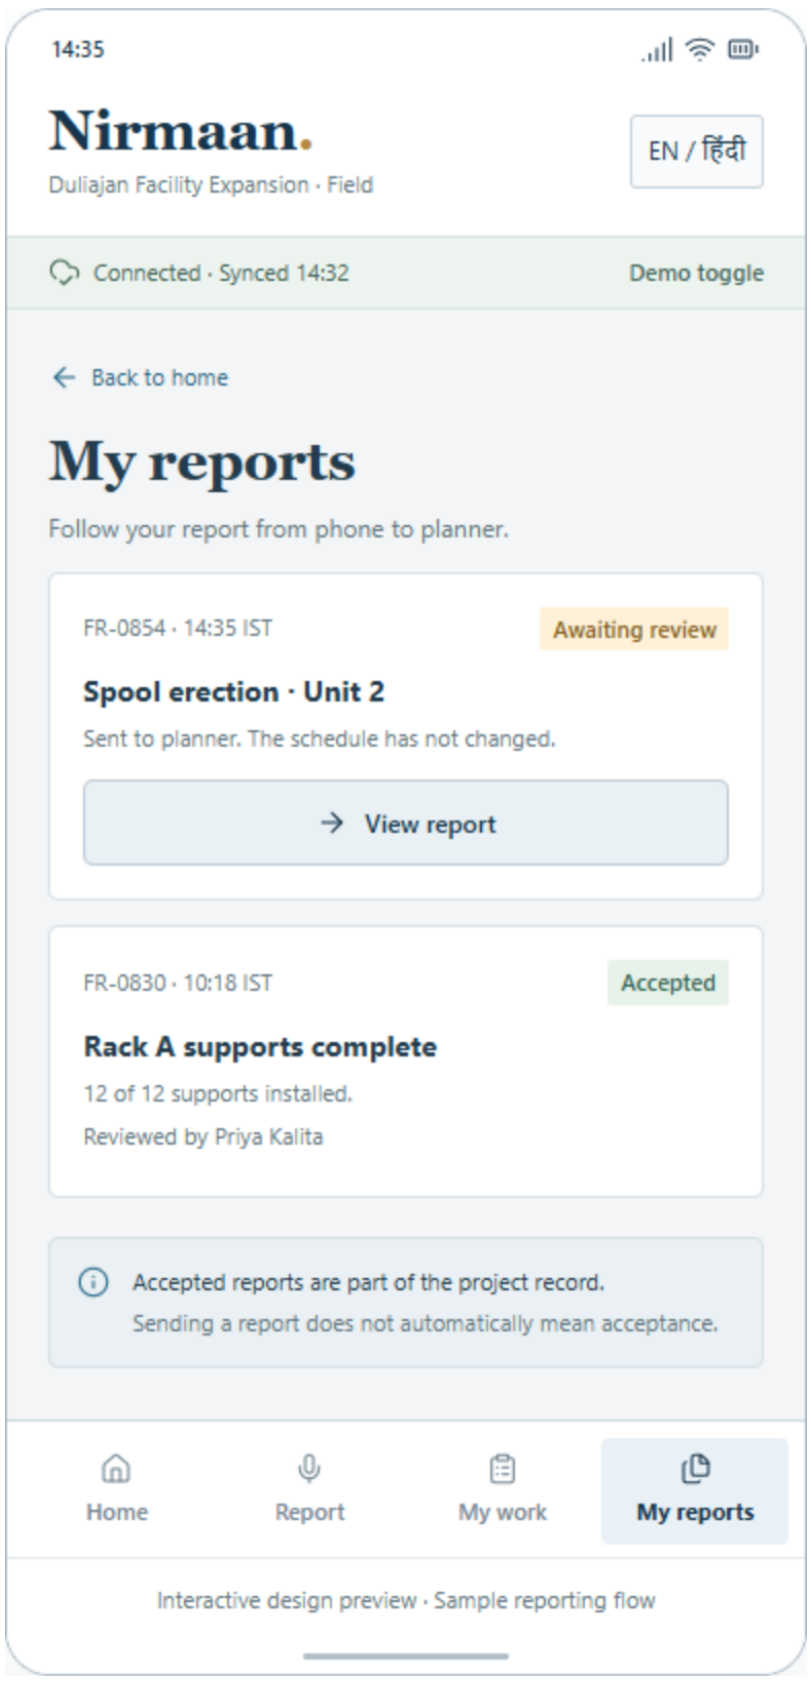

Do not hide connectivity

The field user sees whether the report reached the planner. The design includes a saved-report queue and an explicit sync action.

Keep acceptance distinct

A sent report can still await review. Offline saving and synchronization are interface simulations in this design preview.


Language and supporting evidence

Offer familiar labels and another way to explain the work.

01 Hindi interface



02 Photo evidence

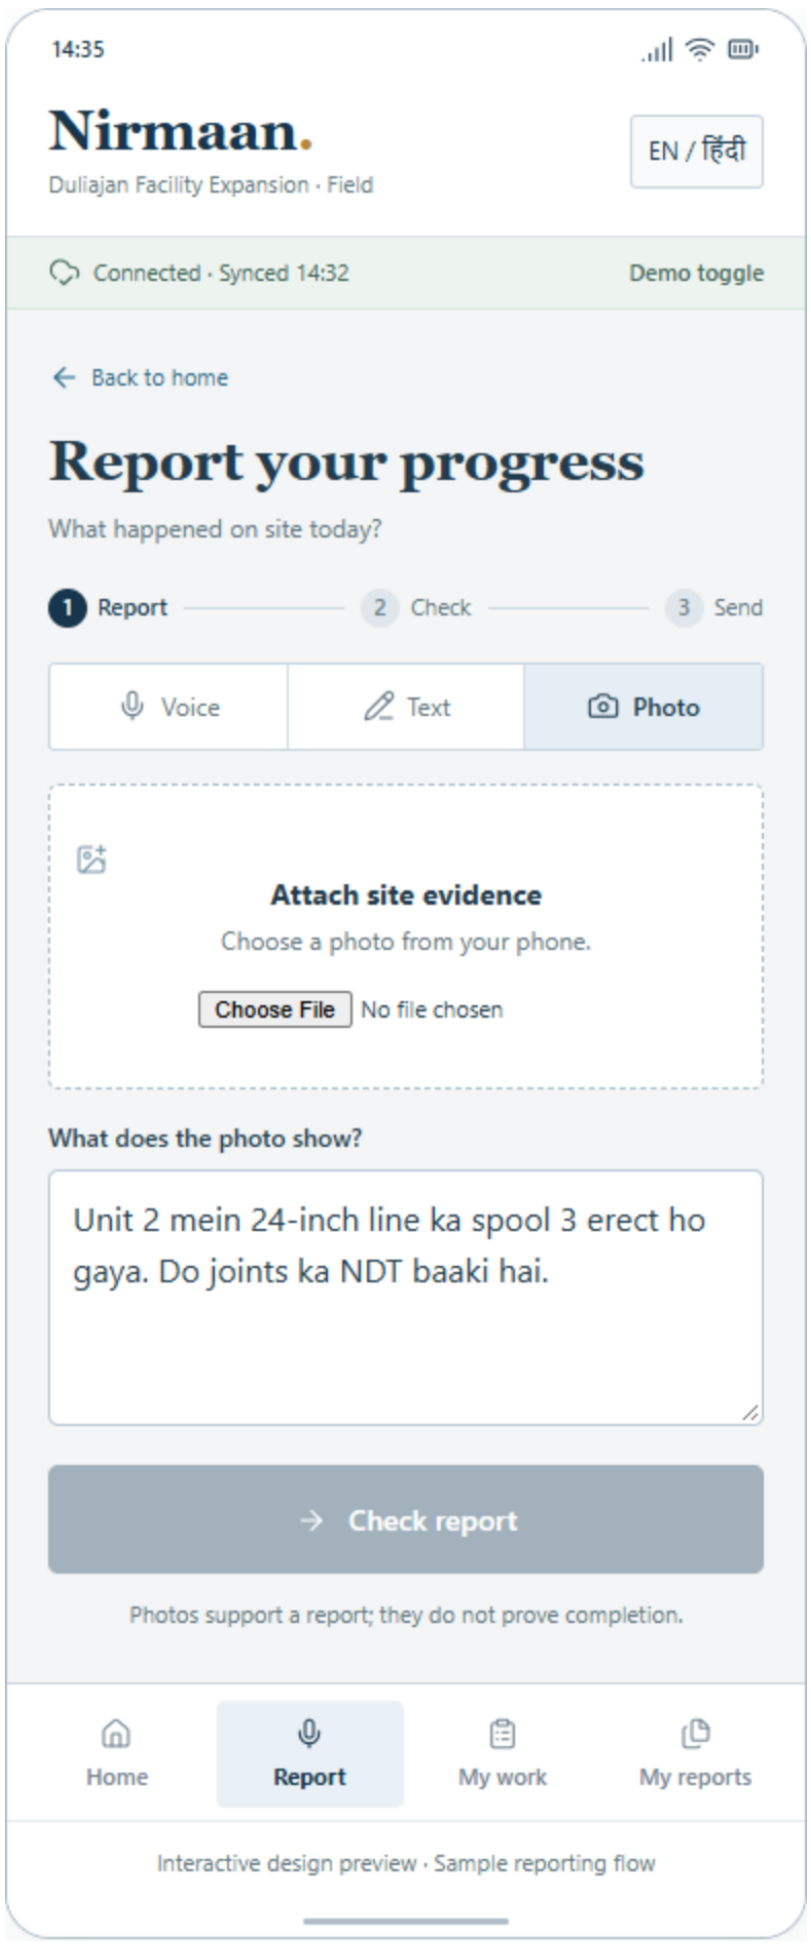

Language is a usability choice

English and Hindi labels are included in the preview. Field testing should verify wording, comprehension and touch targets.

A photo needs context

Ask what the image shows and retain the original report. Selecting a photo in this preview does not upload it or prove completion.

What this direction establishes

A visual baseline for team review before application implementation.

01 Institutional, not ornamental

A formal masthead, horizontal desktop navigation, restrained navy and thin table rules. Serif headings add character; sans-serif labels keep records readable.

02 The report-to-record workflow

Capture evidence, check its meaning, resolve an uncertain activity link, accept the event and retain an audit trail. Field reporting and planning have different views of the same intended workflow.

03 Honest states and dates

Missing dates stay unknown. Partial physical work is distinct from activity completion. Saved, sent, accepted and externally synchronized states must remain separate.

04 Prototype boundaries

These pages document a static concept with fictional data. The interactive previews simulate voice and sync, and are not connected to one another, a database or Primavera. Schedule dependencies and forecasts are not calculated.

05 What to review with the team

Agree on the top navigation and terminology; walk through the ambiguous report and offline states; validate the mobile wording with field users. Then translate the agreed screens into implementation tasks.

REFERENCE BASIS

User-provided desktop references: s1.png to s7.png. Mobile references: sm1.png to sm3.png. Friend-prepared reference: Nirmaan-Three-Design-Options.pdf, especially its Department Register direction. The user’s request for top navigation takes precedence over alternative layouts in that document.

Prepared for the BITS Pilani team. All project, personnel and report records shown are illustrative. No official affiliation or deployment is implied.
